



New Fire Station Thompsonville Fire District #2

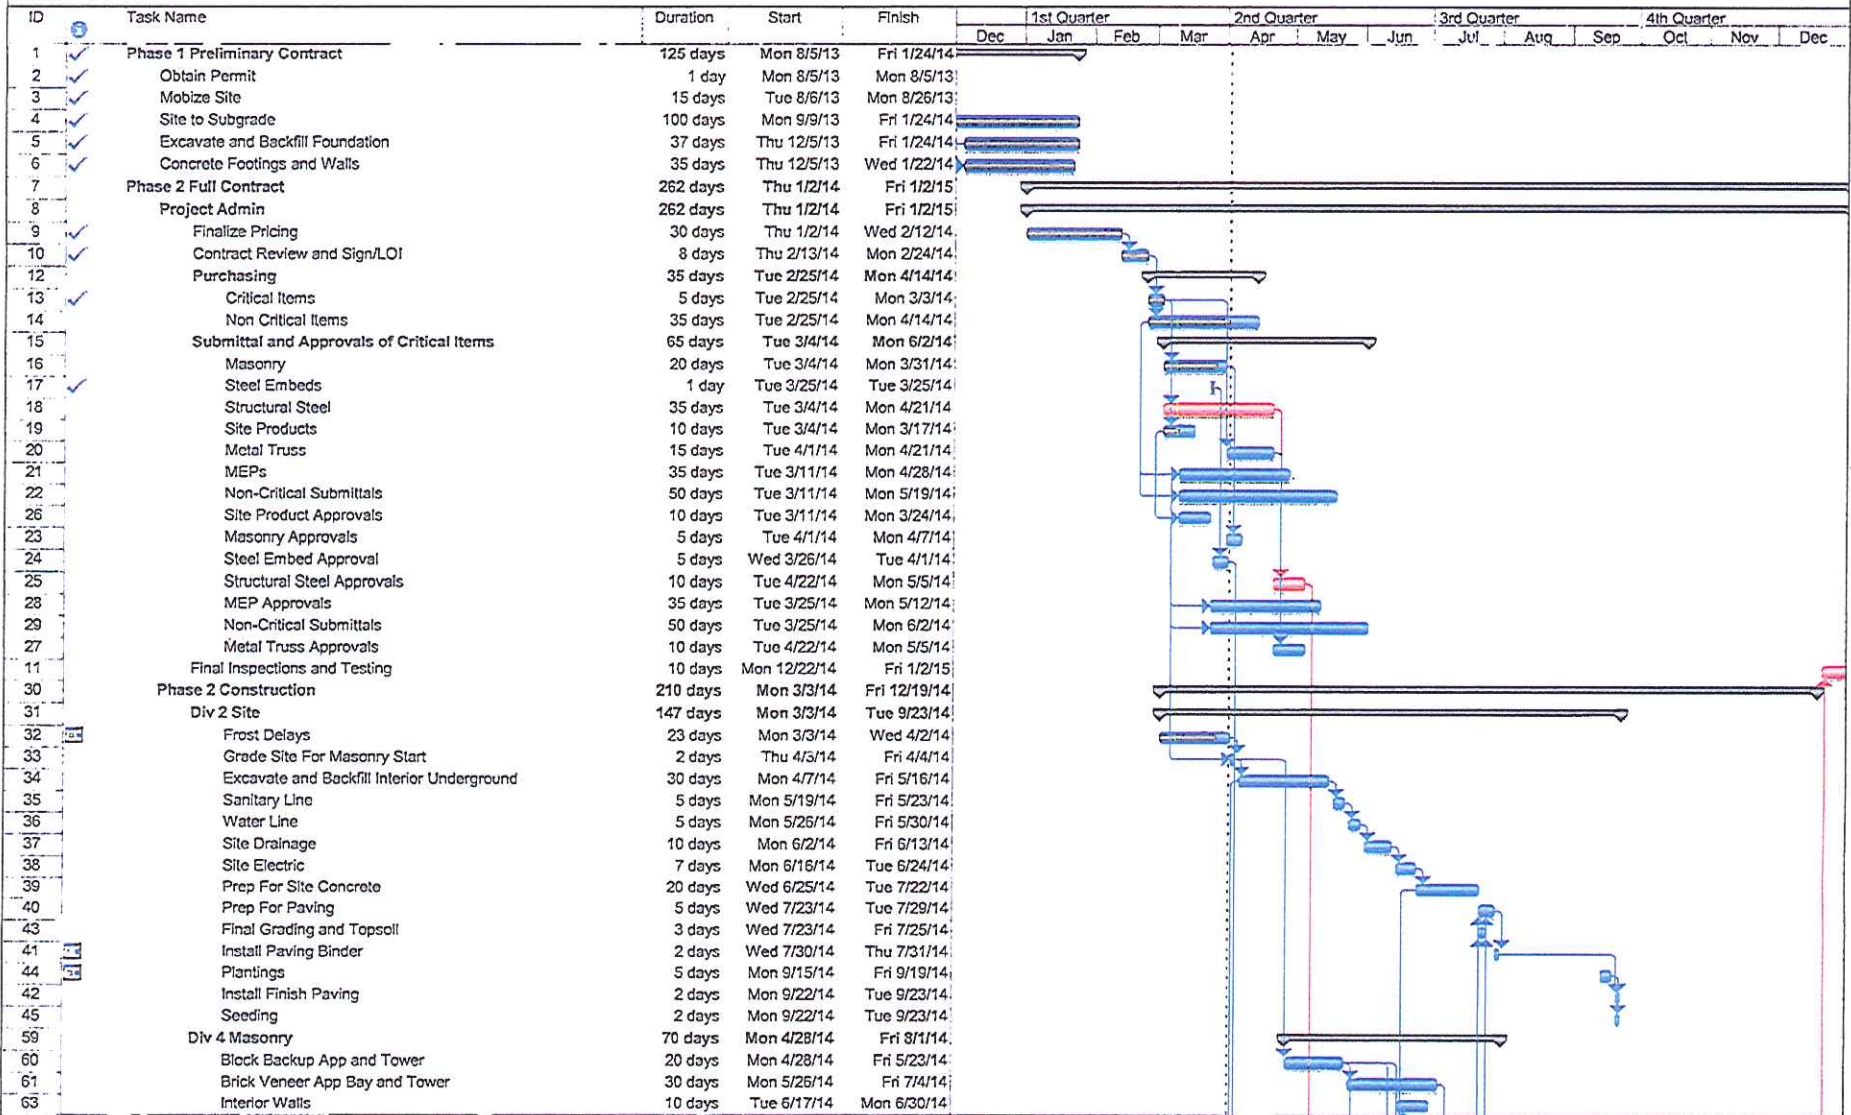

Project: Thompsonville Project Schedu Date: Wed 4/2/14	Task	Summary	Rolled Up Progress	Group By Summary
Critical Task	Rolled Up Task	Split	Deadline	
Progress	Rolled Up Critical Task	External Tasks		
Milestone	Rolled Up Milestone	Project Summary		

New Fire Station Thompsonville Fire District #2

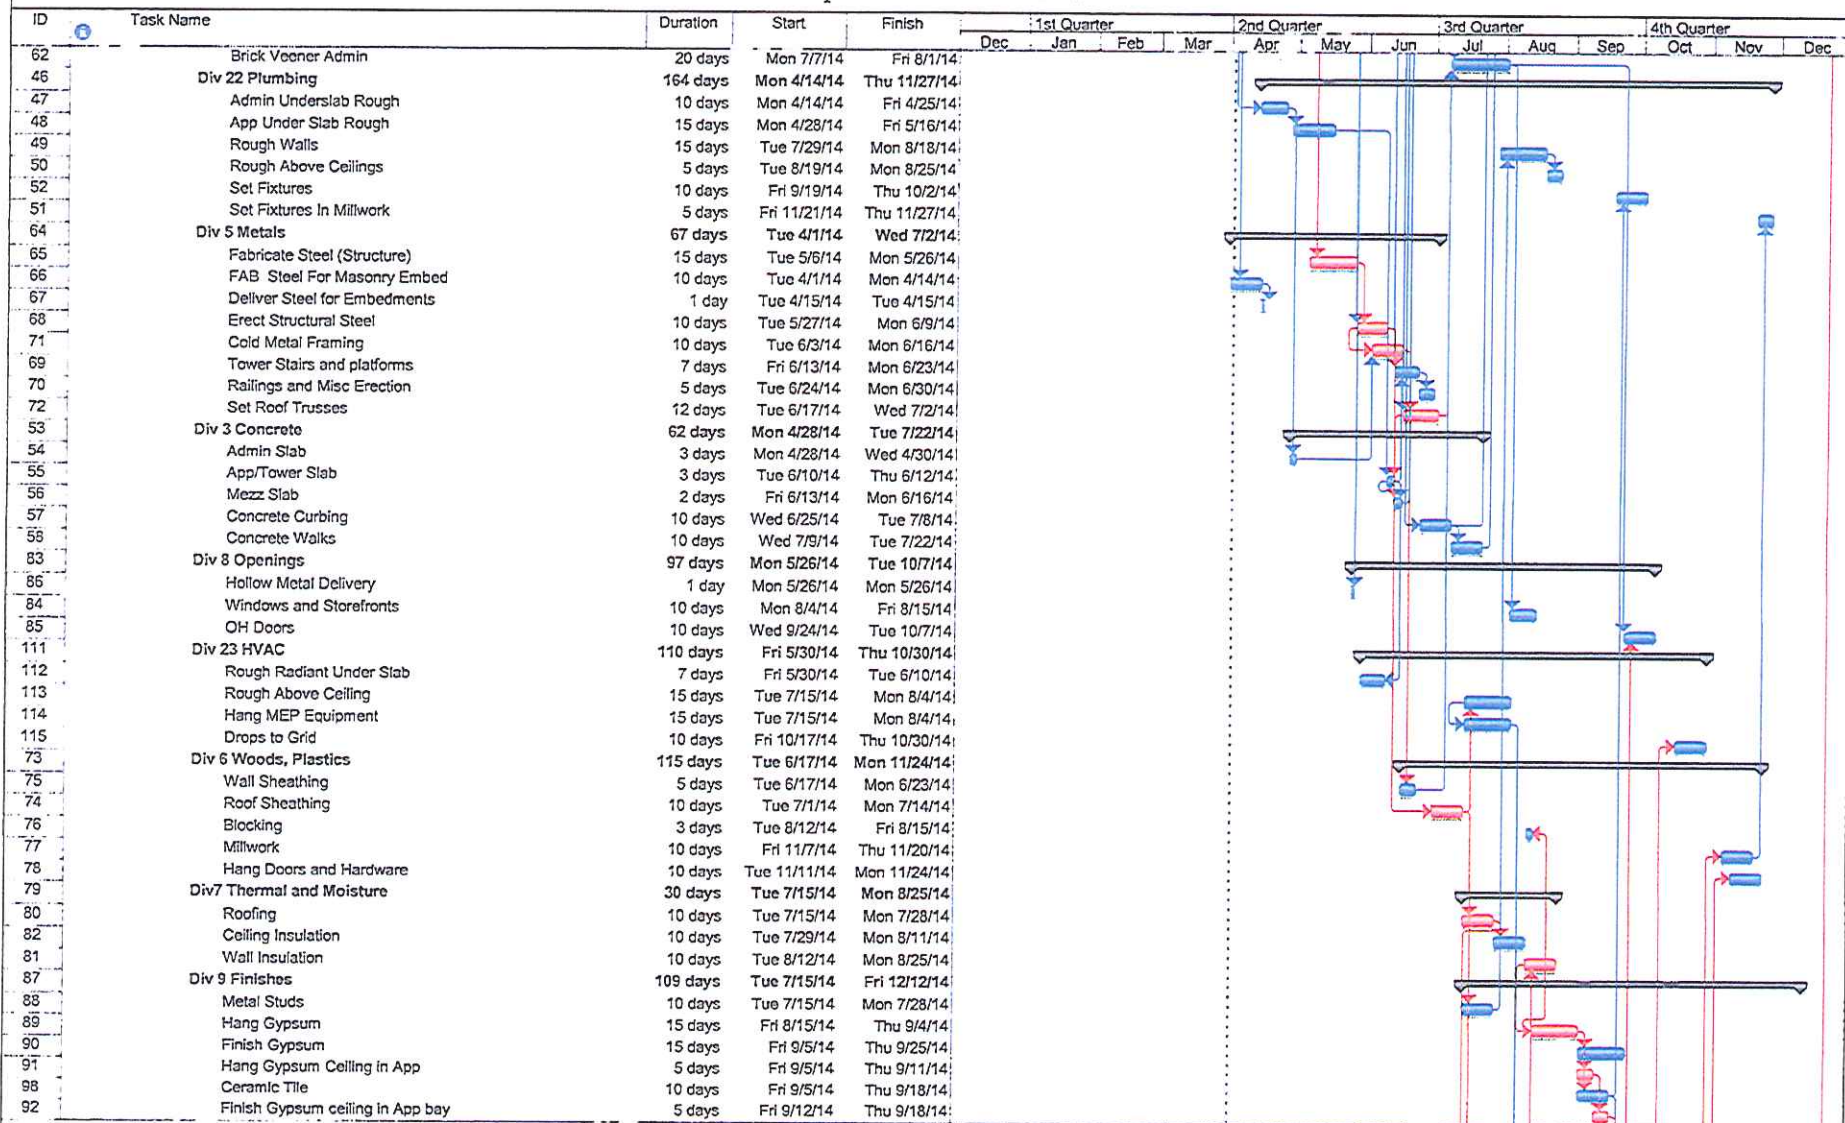

Project: Thompsonville Project Schedu Date: Wed 4/2/14	Task		Summary		Rolled Up Progress		Group By Summary
	Critical Task		Rolled Up Task		Split		Deadline
	Progress		Rolled Up Critical Task		External Tasks		
	Milestone		Rolled Up Milestone		Project Summary		

New Fire Station Thompsonville Fire District #2

ID	Task Name	Duration	Start	Finish	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			
					Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
93	Prime Paint and First Coat Gypsum ceiling in App bay	3 days	Fri 9/19/14	Tue 9/23/14													
94	Prime Paint and First Coat	10 days	Wed 9/24/14	Tue 10/7/14													
95	ACT Grid	15 days	Fri 9/26/14	Thu 10/16/14													
96	ACT Cuts	5 days	Fri 10/17/14	Thu 10/23/14													
97	ACT Field Tile	15 days	Fri 11/7/14	Thu 11/27/14													
99	VCT and Carpet	15 days	Mon 11/10/14	Fri 11/28/14													
100	Finish Coat Paint	10 days	Mon 12/1/14	Fri 12/12/14													
105	Div 22 Fire Suppression	90 days	Tue 7/15/14	Mon 11/17/14													
106	Construct Riser	5 days	Tue 7/15/14	Mon 7/21/14													
107	Rough piping Above Ceiling	15 days	Tue 7/15/14	Mon 8/4/14													
108	Drops in ACT Grid	10 days	Fri 10/24/14	Thu 11/6/14													
109	Testing	2 days	Fri 11/7/14	Mon 11/10/14													
110	Heads	5 days	Tue 11/11/14	Mon 11/17/14													
116	Div 26 Electrical	109 days	Tue 7/22/14	Fri 12/19/14													
117	Rough walls and ceilings	15 days	Tue 7/22/14	Mon 8/11/14													
119	MEP connections	10 days	Tue 8/5/14	Mon 8/18/14													
120	Set Switch Gear and panels	10 days	Tue 7/22/14	Mon 8/4/14													
121	Install Secondaries	3 days	Tue 8/5/14	Thu 8/7/14													
122	Energize	2 days	Fri 8/8/14	Mon 8/11/14													
118	Drops in Grid	15 days	Fri 10/17/14	Thu 11/6/14													
123	Plug/ Switch/Misc equipment	15 days	Mon 12/1/14	Fri 12/19/14													
124	Div 28 Electronic Safety and Security	104 days	Tue 7/22/14	Fri 12/12/14													
125	Rough	10 days	Tue 7/22/14	Mon 8/4/14													
126	Trim and activate	10 days	Mon 12/1/14	Fri 12/12/14													
101	Div 10 Specialties	63 days	Fri 9/19/14	Tue 12/16/14													
102	Toilet Partitions	5 days	Fri 9/19/14	Thu 9/25/14													
103	Toilet Accessories	3 days	Fri 9/26/14	Tue 9/30/14													
104	Signs	2 days	Mon 12/15/14	Tue 12/16/14													

Project: Thompsonville Project Schedu
Date: Wed 4/2/14

Task		Summary		Rolled Up Progress		Group By Summary	
Critical Task		Rolled Up Task		Split		Deadline	
Progress		Rolled Up Critical Task		External Tasks			
Milestone		Rolled Up Milestone		Project Summary			
